



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	March Mar	April Apr	May May	June Jun	July Jul	August Aug	September Sep	October Oct	November Nov
1		Construction Schedule	182 days	Mon 3/4/24	Mon 11/18/24			[Gantt bar]								
2		McMann Complex	182 days	Mon 3/4/24	Mon 11/18/24			[Gantt bar]								
3		McMann Sitework	182 days	Mon 3/4/24	Mon 11/18/24			[Gantt bar]								
4		Mobilization	1 day	Mon 3/4/24	Mon 3/4/24		Mobilization	[Gantt bar]								
5		Temporary Erosion	1 day	Tue 3/5/24	Tue 3/5/24	4	Temporary Erosion	[Gantt bar]								
6		Clearing Proposed Building Lot	15 days	Wed 3/6/24	Tue 3/26/24	5	Clearing Proposed	[Gantt bar]								
7		Excavation of Foundation	10 days	Wed 3/27/24	Tue 4/9/24	6	Excavation of Foundation	[Gantt bar]								
8		Form & Pour Foundation Footing	10 days	Wed 4/10/24	Tue 4/23/24	7	Form& Pour Foundation	[Gantt bar]								
9		Form & Pour Foundation Walls	15 days	Wed 4/24/24	Tue 5/14/24	8	Form& Pour Foundation Walls	[Gantt bar]								
10		Install Foundation Drainage & Backfill	1 wk	Wed 5/15/24	Tue 5/21/24	9	Install Foundation	[Gantt bar]								
11		Excavate Underslab MEP's	1 wk	Wed 5/22/24	Wed 5/29/24	10	Excavate Underslab MEP's	[Gantt bar]								
12		Underslab Rough In	10 days	Thu 5/30/24	Wed 6/12/24	11	Underslab Rough	[Gantt bar]								
13		Backfill Slab	2 days	Thu 6/13/24	Fri 6/14/24	12	Backfill Slab	[Gantt bar]								
14		Set and Pour Slab	1 wk	Mon 6/17/24	Fri 6/21/24	13	Set and Pour Slab	[Gantt bar]								
15		Demolition of Existing Services	6 days	Thu 5/30/24	Thu 6/6/24	11	Demolition of Existing Services	[Gantt bar]								
16		Dig For New Services To Building	2 wks	Fri 6/7/24	Thu 6/20/24	15	Dig For New Services To	[Gantt bar]								
17		Install Underground Utilities	1 wk	Fri 6/21/24	Thu 6/27/24	16	Install Underground	[Gantt bar]								
18		Backfill Trench	1 wk	Fri 6/28/24	Fri 7/5/24	17	Backfill Trench	[Gantt bar]								
19		Prep for Concrete Pads	3 days	Mon 7/8/24	Wed 7/10/24	18	Prep for Concrete	[Gantt bar]								
20		Pour Concrete Pads	2 days	Thu 7/11/24	Fri 7/12/24	19	Pour Concrete Pa	[Gantt bar]								
21		Install Oil Water Separator	3 days	Mon 7/15/24	Wed 7/17/24	20	Install Oil Water Separator	[Gantt bar]								
22		Install Focal Point	3 days	Thu 7/18/24	Mon 7/22/24	21	Install Focal Point	[Gantt bar]								
23		Install Pump Station	3 days	Tue 7/23/24	Thu 7/25/24	22	Install Pump Stati	[Gantt bar]								
24		Demolition of Bathroom and Shed	4 days	Fri 7/26/24	Wed 7/31/24	23	Demolition of Existing Building	[Gantt bar]								
25		Demolition of Existing Facility	1 day	Mon 11/18/24	Mon 11/18/24	46	Demolition of Existing Facility	[Gantt bar]								
26		Base Pave	1 day	Thu 9/26/24	Thu 9/26/24	59	Base Pave	[Gantt bar]								
27		Final Pave	1 day	Fri 9/27/24	Fri 9/27/24	60	Final Pave	[Gantt bar]								
28		Striping	1 day	Mon 9/30/24	Mon 9/30/24	61	Striping	[Gantt bar]								

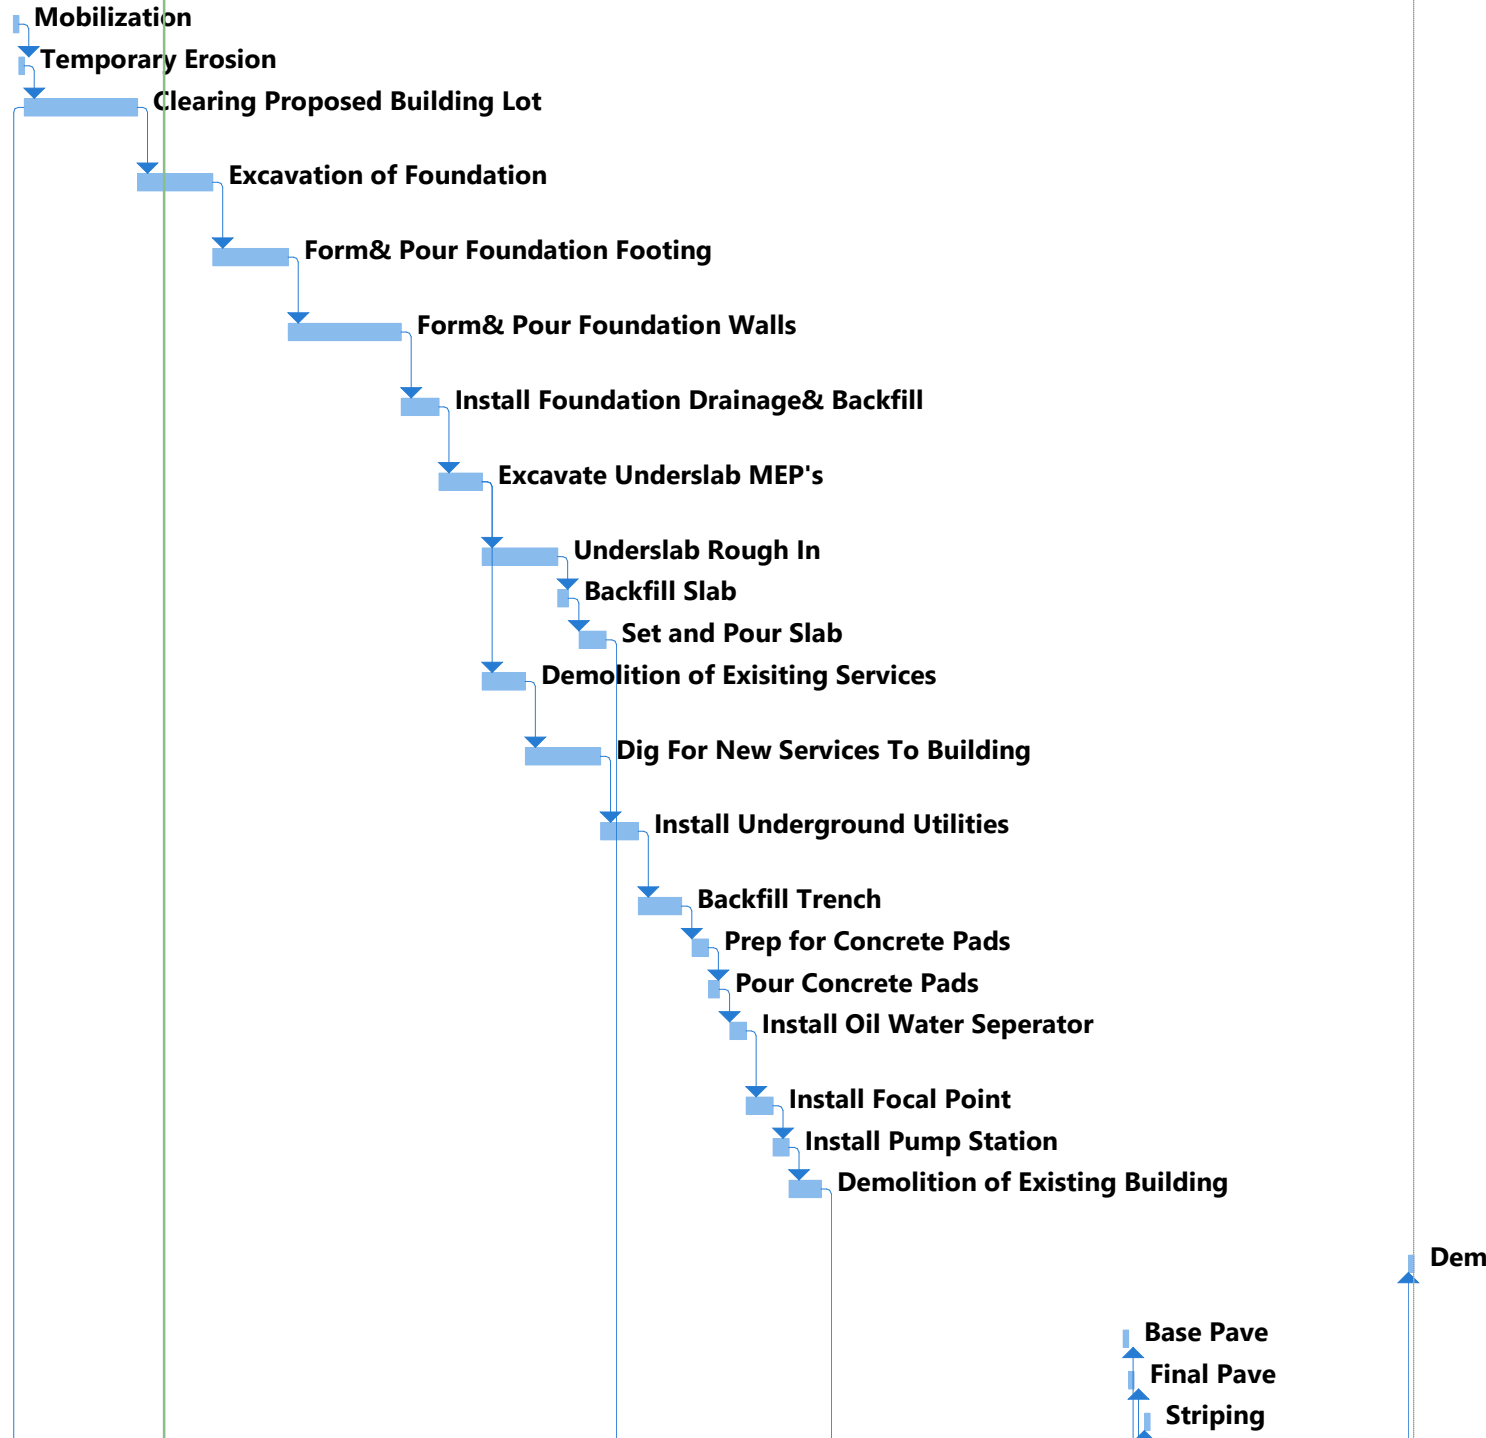

Project: McMann Schedule 4-1-
Date: Mon 4/1/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	March	April	May	June	July	August	September	October	November
								Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
29		Building Envelope	102 days	Mon 6/24/24	Fri 11/15/24		Building Envelope									
30		PEMB Installation	7 wks	Mon 6/24/24	Mon 8/12/24	14	PEMB Installation									
31		Window & Exterior Door Install	3 days	Tue 8/13/24	Thu 8/15/24	30	Window& Exterior									
32		Overhead Door Install	2 wks	Tue 8/13/24	Mon 8/26/24	30	Overhead Door In									
33		Interior Wood Framing	2.5 wks	Tue 8/13/24	Thu 8/29/24	30	Interior Wood Fra									
34		MEP Rough In	2.5 wks	Thu 8/29/24	Tue 9/17/24	33	MEP Rough In									
35		Insulation	3 days	Wed 9/18/24	Fri 9/20/24	34	Insulation									
36		Hang, Mud, & Tape	2.5 wks	Mon 9/23/24	Wed 10/9/24	35	Hang,Mud,& Tape									
37		Prime & 1st Coat	3 days	Wed 10/9/24	Tue 10/15/24	36	Prime& 1st Coat									
38		PVC Wall Lining	2 wks	Tue 10/15/24	Tue 10/29/24	37	PVC Wall Lining									
39		Floor Install	4 days	Tue 10/15/24	Mon 10/21/24	37	Floor Install									
40		Epoxy Install	3 days	Tue 10/15/24	Fri 10/18/24	37	Epoxy Install									
41		Final Paint	3 days	Mon 10/21/24	Thu 10/24/24	39	Final Paint									
42		MEP Finishes	2.5 wks	Thu 10/24/24	Mon 11/11/24	41	MEP Finishes									
43		Interior Door Install	1 day	Thu 10/24/24	Fri 10/25/24	41	Interior Door Inst									
44		Millwork Install	2.5 wks	Mon 10/28/24	Wed 11/13/24	41FS+2 days	Millwork Install									
45		Final Clean	1 day	Thu 11/14/24	Thu 11/14/24	44	Final Clean									
46		CO Inspection	1 day	Fri 11/15/24	Fri 11/15/24	45	CO Inspection									
47		Bath Middle School	20 days	Thu 8/1/24	Wed 8/28/24		Bath Middle Scho									
48		Demo Sidewalk & Curb	2 days	Thu 8/1/24	Fri 8/2/24	24	Demo Sidewalk&									
49		Common Excavation	4 days	Mon 8/5/24	Thu 8/8/24	48	Common Excavat									
50		Install Focal Point	3 days	Fri 8/9/24	Tue 8/13/24	49	Install Focal Point									
51		Install Underground Piping	1 wk	Wed 8/14/24	Tue 8/20/24	50	Install Undergrou									
52		Backfill and Bring Up to Grade	4 days	Wed 8/21/24	Mon 8/26/24	51	Backfill and Bring									
53		Install Curbing and Sidewalk	2 days	Tue 8/27/24	Wed 8/28/24	52	Install Curbing									
54		Tennis Courts	21 days	Thu 8/29/24	Fri 9/27/24		Tennis Courts									
55		Removal of Pavement, Catch Basin, Curb, Storm Drain, and	1 wk	Thu 8/29/24	Thu 9/5/24	53	Removal of Pavement,Catch									
56		Relocate 3/4" Water Main	4 days	Fri 9/6/24	Wed 9/11/24	55	Relocate 3/4"Wat									
57		Install New Drain System	4 days	Thu 9/12/24	Tue 9/17/24	56	Install New Drain									
58		Install Focal Points	4 days	Wed 9/18/24	Mon 9/23/24	57	Install Focal Point									
59		Bring Site Up To Grade	2 days	Tue 9/24/24	Wed 9/25/24	58	Bring Site Up To G									
60		Base Pave	1 day	Thu 9/26/24	Thu 9/26/24	59	Base Pave									
61		Final Pave	1 day	Fri 9/27/24	Fri 9/27/24	60	Final Pave									
62		Oak Grove	30.5 days	Mon 3/11/24	Mon 4/22/24		Oak Grove									
63		Clear Existing Site	1.5 wks	Mon 3/11/24	Wed 3/20/24	6SS+3 days	Clear Existing Site									

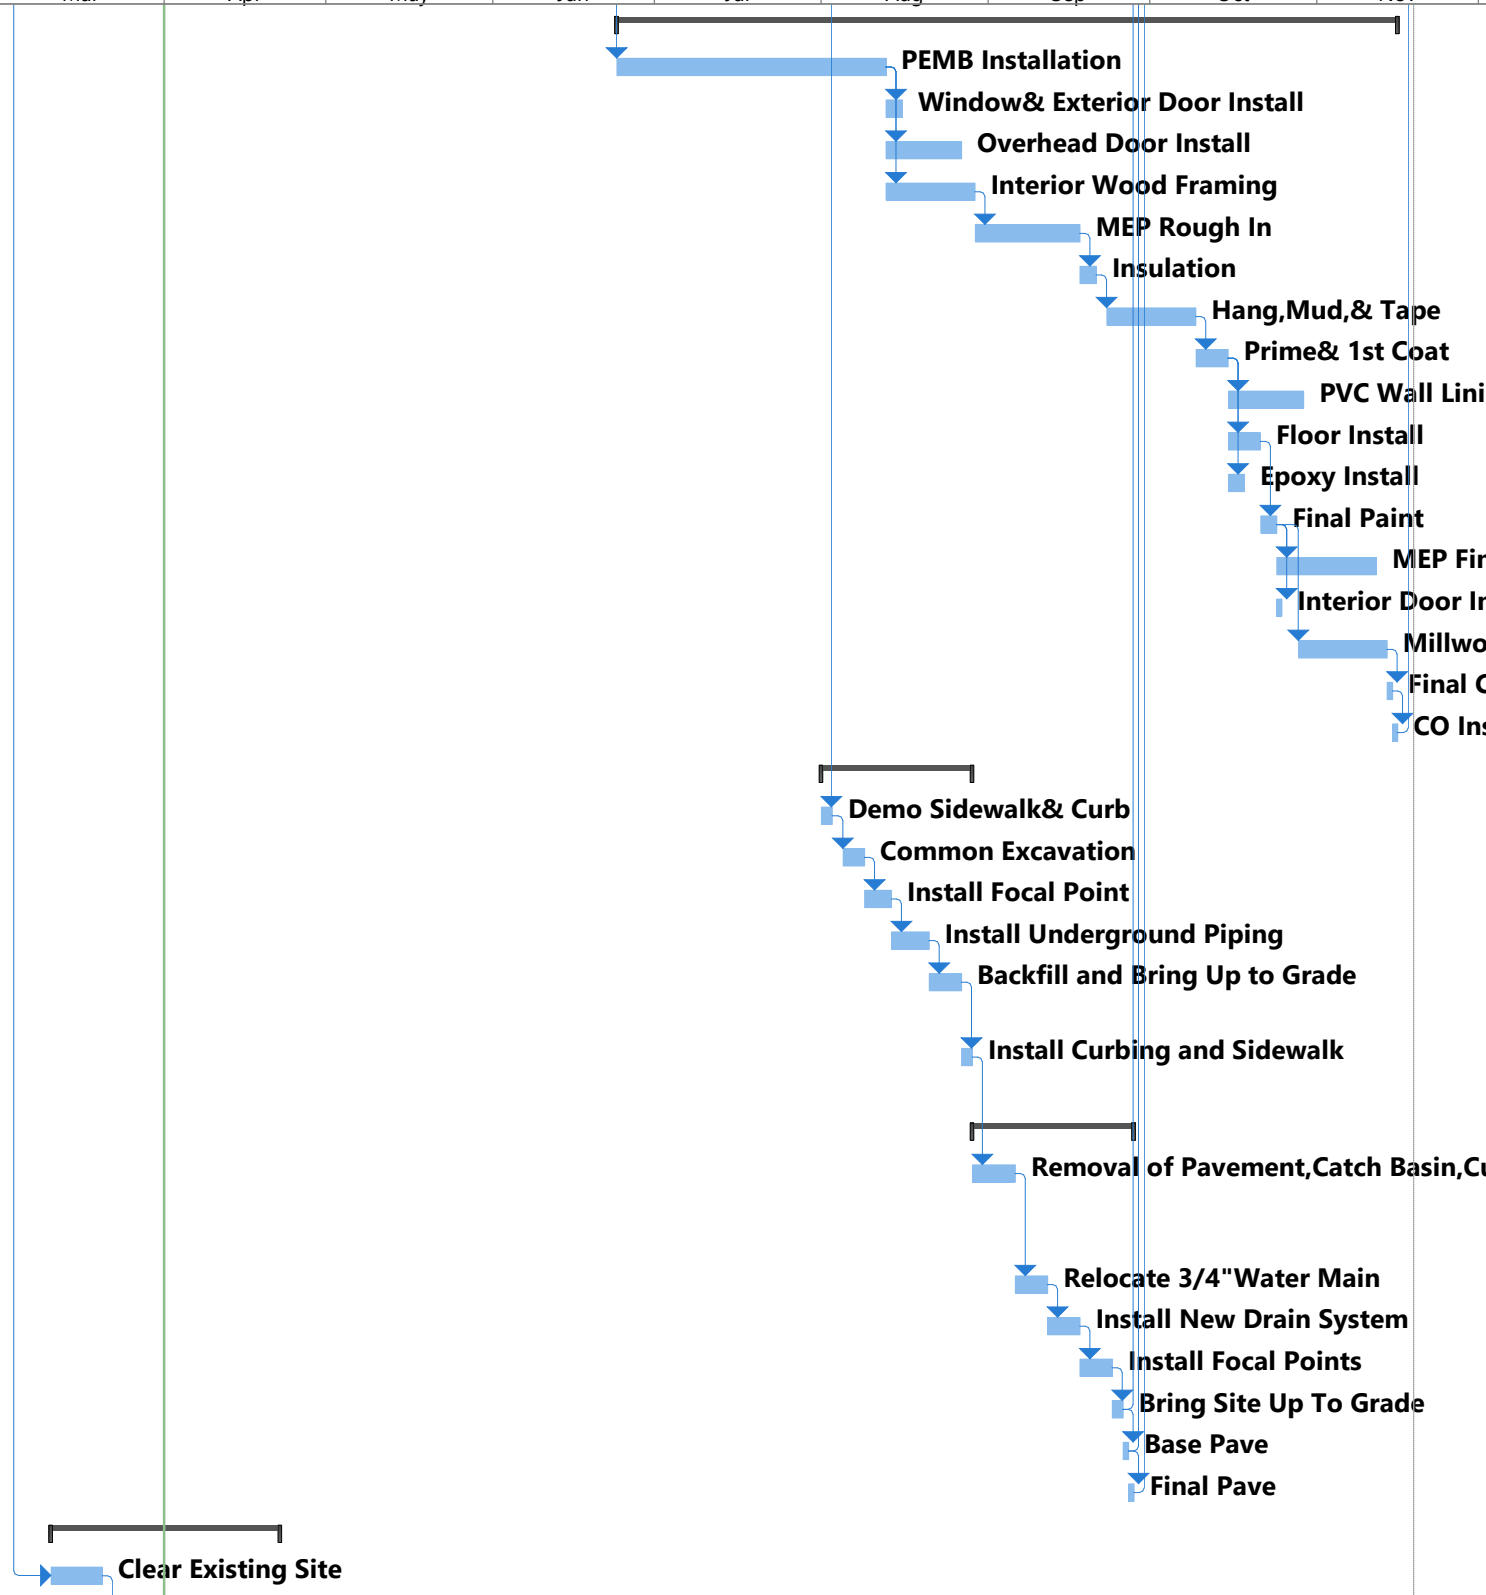

Project: McMann Schedule 4-1-
Date: Mon 4/1/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Gantt Chart											
								March	April	May	June	July	August	September	October	November			
64		Excavate Detention Pond 1 and Associated	4 days	Wed 3/20/24	Tue 3/26/24	63	Excavate Detention Pond	Excavate Detention Pond 1 and Associated Piping											
65		Bring Detention Pond 1 Up to Grade and Loam & Seed	1 wk	Tue 3/26/24	Tue 4/2/24	64	Bring Detention Pond 1 Up to Grade and	Bring Detention Pond 1 Up to Grade and Loam& Seed											
66		Excavate GUSF1	5 days	Fri 3/22/24	Fri 3/29/24	64SS+2 days	Excavate GUSF1	Excavate GUSF1											
67		Bring GUSF1 Up to Grade, Install Rip Rap, and Loam & Seed	1 wk	Fri 3/29/24	Fri 4/5/24	66	Bring GUSF1 Up to Grade,Install Rip Rap,and	Bring GUSF1 Up to Grade,Install Rip Rap,and Loam& Seed											
68		Excavate GUSF2	5 days	Mon 3/25/24	Mon 4/1/24	66SS+1 day	Excavate GUSF2	Excavate GUSF2											
69		Bring GUSF2 Up to Grade, Install Rip Rap, and Loam & Seed	1 wk	Mon 4/1/24	Mon 4/8/24	68	Bring GUSF2 Up to Grade,Install Rip Rap,and	Bring GUSF2 Up to Grade,Install Rip Rap,and Loam& Seed											
70		Install Stone Level Spreader & Rip Rap	2 days	Mon 4/8/24	Wed 4/10/24	69	Install Stone Level Spreader&	Install Stone Level Spreader& Rip Rap											
71		Install Drain Piping	8 days	Wed 4/10/24	Mon 4/22/24	70		Install Drain Piping											

Project: McMann Schedule 4-1- Date: Mon 4/1/24	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
