| Activity ID | Activity Description | Orig Dur | Remaining Duration | Early Start | Early Finish | Total Float |
|---|---|---|---|---|---|---|
| **MeDOT Paul Davis Memorial Bridge** | | | | | | |
| **Preconstruction** | | | | | | |
| 1000 | Preconstruction Meeting | 0 | 0 | 07/13/20 | | 0 |
| 1005 | Project Start | 0 | 0 | 07/13/20 | | 0 |
| 1010 | Approach Signs | 1 | 1 | 07/13/20 | 07/14/20 | 5d |
| **Erosion Control** | | | | | | |
| 2000 | Install Temporary Controls | 1 | 1 | 07/13/20 | 07/14/20 | 91d |
| 2005 | Remove Temporary Controls | 1 | 1 | 09/18/20 | 09/21/20 | 43d |
| **Detours** | | | | | | |
| 3000 | Prep for Signals | 7 | 7 | 07/13/20 | 07/22/20 | 4d |
| 3005 | Install Detour Signs | 5 | 5 | 07/14/20 | 07/21/20 | 5d |
| 3010 | Install Traffic & PED Signals | 2 | 2 | 07/22/20 | 07/24/20 | 4d |
| 3015 | Pavement Markings | 1 | 1 | 07/24/20 | 07/27/20 | 4d |
| 3020 | Remove Signals | 2 | 2 | 10/07/20 | 10/09/20 | 28d |
| 3025 | Remove Detour Signs | 3 | 3 | 10/07/20 | 10/12/20 | 28d |
| **High Street Bridge & Approaches** | | | | | | |
| 4000 | Install Phase I Traffic Controls | 1 | 1 | 07/27/20 | 07/28/20 | 4d |
| 4005 | Demo Phase I Bridge Wearing Surface | 5 | 5 | 07/28/20 | 08/04/20 | 4d |
| 4010 | Phase I Bridge Deck Repairs | 5 | 5 | 08/04/20 | 08/11/20 | 4d |
| 4015 | Phase I Bridge Wearing Surface Install & | 15 | 15 | 08/11/20 | 09/01/20 | 4d |
| 4020 | Phase I Bridge Sidewalk Repairs | 2 | 2 | 08/11/20 | 08/13/20 | 17d |
| 4025 | Install Phase II Traffic Controls | 1 | 1 | 09/01/20 | 09/02/20 | 4d |
| 4030 | Demo Phase II Bridge Wearing Surface | 5 | 5 | 09/02/20 | 09/09/20 | 4d |
| 4035 | Phase II Deck Repairs | 5 | 5 | 09/09/20 | 09/16/20 | 4d |
| 4040 | Approach Sidewalk Construction | 5 | 5 | 09/09/20 | 09/16/20 | 18d |

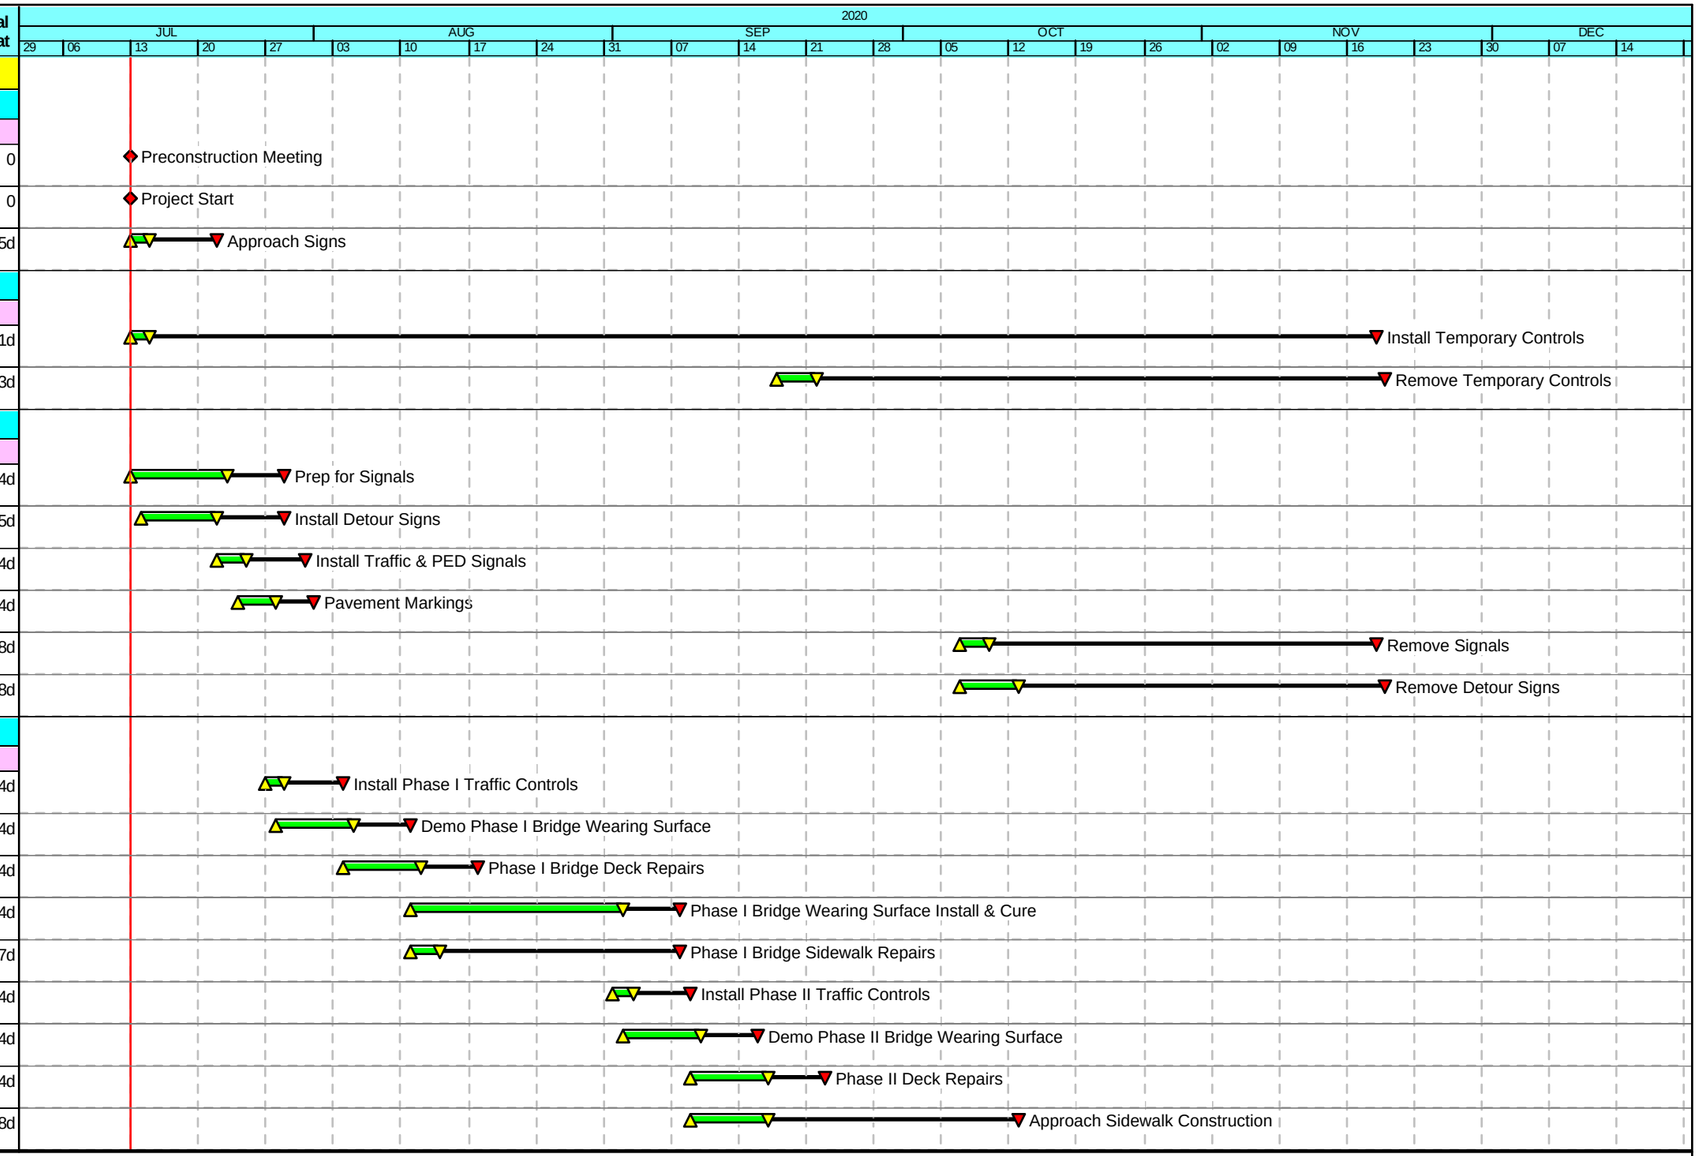


| | |
|---|---|
| Start date | 07/13/20 11:00AM |
| Finish date | 11/20/20 8:59AM |
| Data date | 07/13/20 11:00AM |
| Run date | 07/01/20 2:00PM |
| Page number | 1A |

© Primavera Systems, Inc.

**MeDOT Paul Davis Memorial Bridge**

- Early start point
- Early finish point
- Early bar
- Total float point
- Total float bar
- Target start point
- Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- Progress point
- Critical point
- Summary point
- Start milestone point
- Finish milestone point

| Activity ID | Activity Description | Orig Dur | Remaining Duration | Early Start | Early Finish | Total Float |
|---|---|---|---|---|---|---|
| 4045 | Phase II Bridge Wearing Surface Install & | 15 | 15 | 09/16/20 | 10/07/20 | 4d |
| 4050 | Phase II Bridge Sidewalk Repairs | 2 | 2 | 09/16/20 | 09/18/20 | 33d |
| 4055 | Approach Curb Installation | 1 | 1 | 09/16/20 | 09/17/20 | 18d |
| 4060 | Install HMA Pavement - Hand Placed | 1 | 1 | 09/17/20 | 09/18/20 | 18d |
| 4065 | Abutment Repairs | 10 | 10 | 09/18/20 | 10/02/20 | 33d |
| 4070 | Mill Existing Bituminous Paving | 1 | 1 | 10/07/20 | 10/08/20 | 4d |
| 4075 | Install HMA Pavement - Machine Placed | 1 | 1 | 10/08/20 | 10/09/20 | 4d |
| 4080 | Sawcut Grooving | 1 | 1 | 10/09/20 | 10/12/20 | 26d |
| 4085 | Pavement Markings | 1 | 1 | 10/12/20 | 10/13/20 | 26d |
| 4090 | HMA Surface Pavement Deadline | 0 | 0 | | 10/15/20 | 0 |
| **Project Closeout** | | | | | | |
| 5000 | Clean-Up & Punch List | 1 | 1 | 10/13/20 | 10/14/20 | 26d |
| 5005 | Remove Approach Signs | 1 | 1 | 10/14/20 | 10/15/20 | 26d |
| 5010 | Anticipated Project Completion Date | 0 | 0 * | | 10/15/20 | 26d |
| 5015 | Project Completion Date | 0 | 0 | 11/20/20 | | 0 |
| | | 94 | 94 | 07/13/20 | 11/20/20 | 0 |

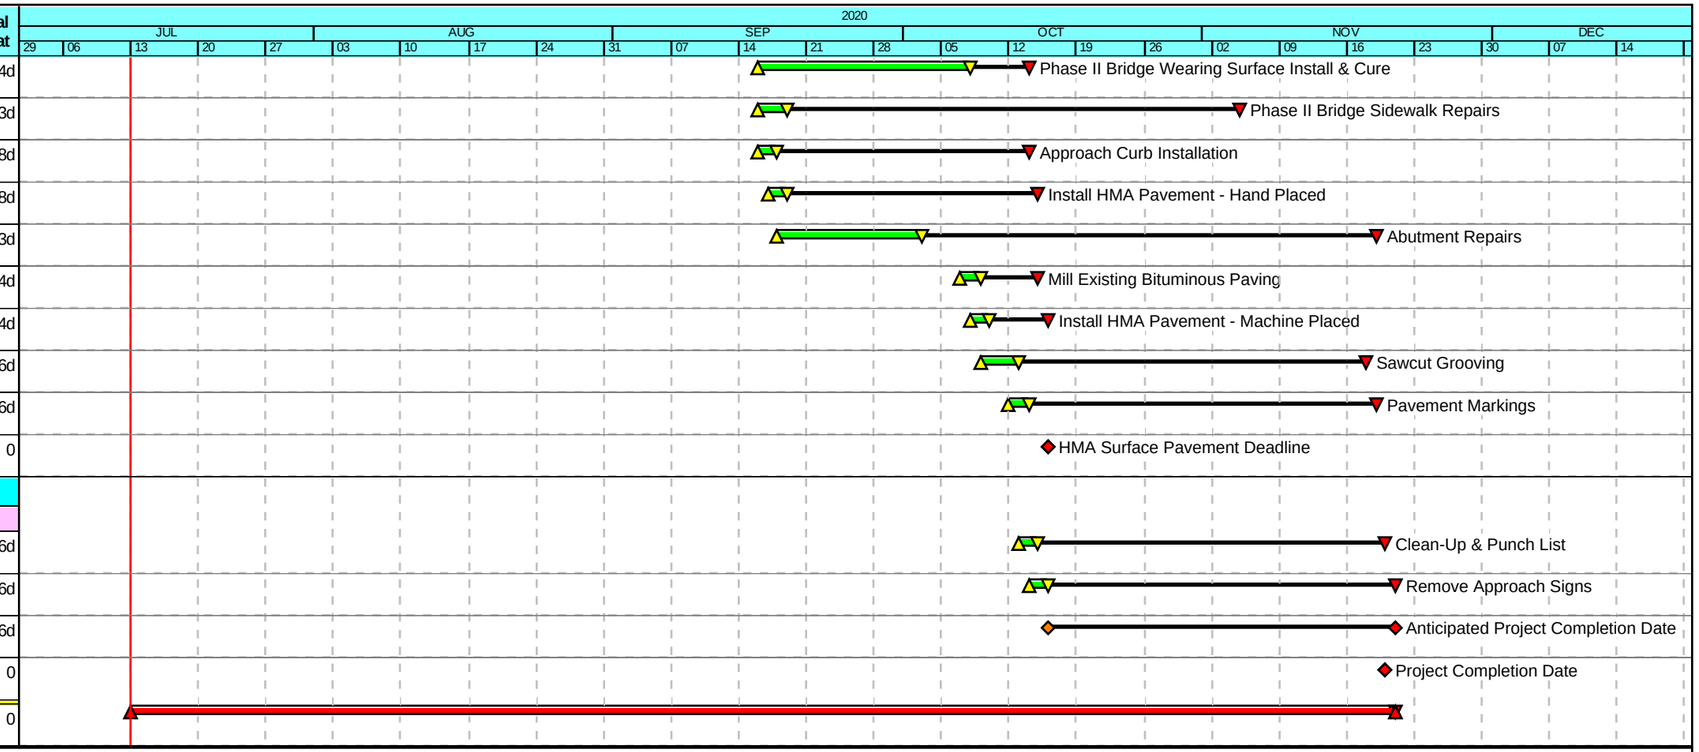


| | |
|---|---|
| Start date | 07/13/20 11:00AM |
| Finish date | 11/20/20 8:59AM |
| Data date | 07/13/20 11:00AM |
| Run date | 07/01/20 2:00PM |
| Page number | 2A |

© Primavera Systems, Inc.

**MeDOT Paul Davis Memorial Bridge**

- Early start point
- Early finish point
- Early bar
- Total float point
- Total float bar
- Target start point
- Target finish point
- Target bar
- Progress bar
- Critical bar
- Summary bar
- Progress point
- Critical point
- Summary point
- Start milestone point
- Finish milestone point
